Kakebe

PROPOSAL

Digital Platform for the Lango Cultural Foundation

Website · Admin Control Panel · Lango Mobile App

PREPARED FOR
Lango Cultural Foundation


PREPARED BY
Kakebe Technologies Limited
Lira City, Uganda

DATE
26 October 2026

VERSION
1.1 (draft for discussion)

DELIVERY
3 months, from signed agreement to launch

COMPANION DOCUMENT
Financial Proposal (separate)

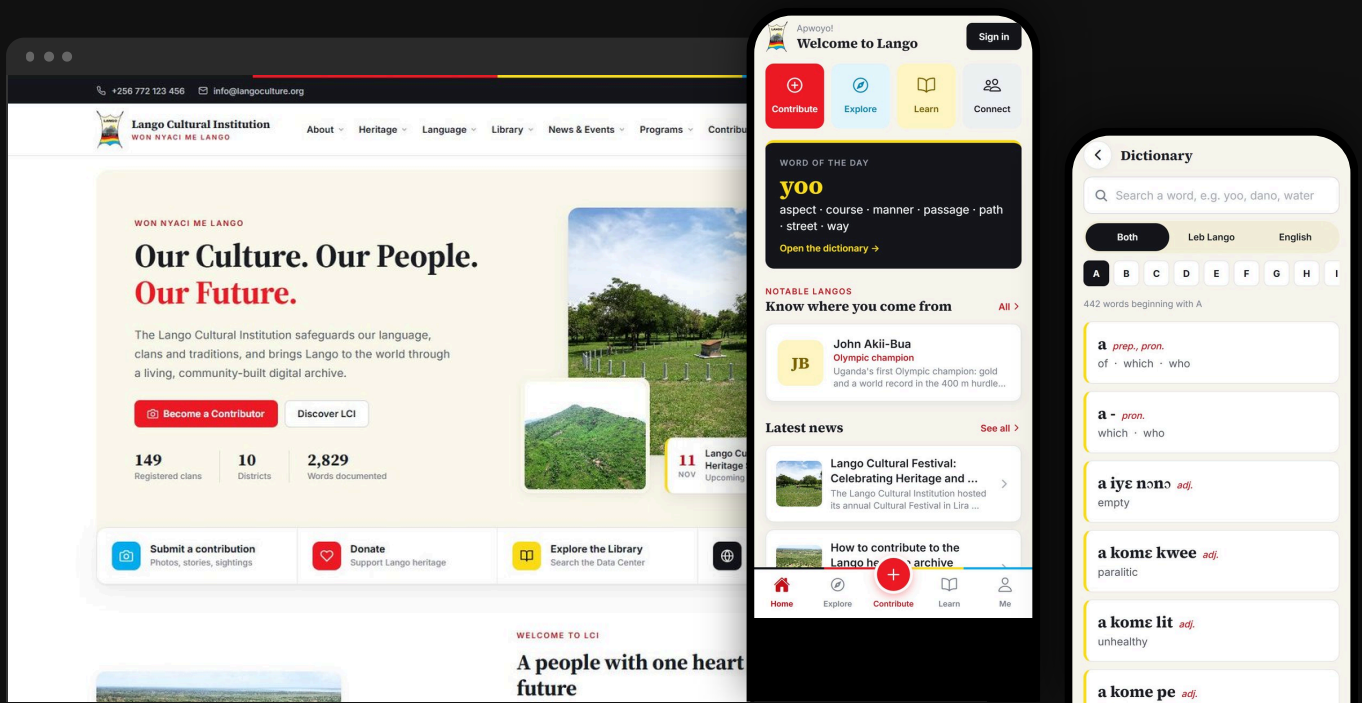

CONTENTS AND DOCUMENT CONTROL

Contents

1 Executive Summary 3
2 The Foundation's Needs and Our Approach 4
3 One Platform, Three Surfaces 5
4 The Public Website 6
5 The Admin Control Panel 7
6 The Lango Mobile App 8
7 Contribution and Content Governance 9
8 Architecture, Security and Data Protection 10
9 About Kakebe Technologies 11
10 Portfolio and References 12
11 Delivery in Three Months 14
12 Team, Governance, Training and Support 15
13 Risks, Success Measures and Assumptions 16
14 Next Steps and Acceptance 17

Document control

Document	Proposal: Digital Platform for the Lango Cultural Foundation. The financial proposal is a separate document.
Prepared for / by	Lango Cultural Foundation / Kakebe Technologies Limited, Rm B1, Plot 43, Renzo City House, Obote Avenue, Lira City, Uganda
Date and version	26 October 2026 · 1.1 (draft for discussion)
Delivery	Three months from signed agreement to public launch (Chapter 11)
Proposal contact	[TBC: name, title, phone and email]

Reading guide. Decision makers: Chapters 1, 3 and 11. Programme and content teams: Chapters 4 to 7. Technical and legal reviewers: Chapters 8 and 13. Evidence of delivery: Chapters 9 and 10. Text like [TBC: item] marks something to confirm before the proposal is issued as final.

Confidentiality. This document contains commercial and technical information prepared for the Lango Cultural Foundation. It may not be copied or shared outside the Foundation without the written permission of Kakebe Technologies Limited. Names of organisations and products belong to their owners and are used to describe work delivered by Kakebe.

CHAPTER 1

Executive Summary

One platform for the language, clans, history and heritage of the Lango, delivered in three months by a team that has already built a working version.

Lango Cultural Foundation holds a heritage older than any archive: Leb Lango, well over a hundred clans, the oral history of nine districts and Lira City, and the ceremonies, songs and proverbs that tie them together. Much of it still lives in elders' memories, family albums and WhatsApp groups, and some is lost every year, while a phone-first, diaspora-connected generation looks for its culture on a screen. Kakebe Technologies proposes to bring the two together with **one platform made of three connected parts**:

Part	What it is	Who it serves
Public website	A fast, bilingual home for history, districts, clans, heritage, the Language Hub (dictionary, translator, proverbs, lessons), news, events, programmes and giving	Citizens, students, researchers, diaspora, partners, media
Admin control panel	A role-based workspace where the Foundation's own staff publish, review, translate and report, with no developer needed day to day	Editors, moderators, language experts, clan leaders
Lango Mobile App	Android, iOS and installable web app: offline dictionary, guided contribution (GPS, camera, voice), notifications, recognition	Youth, clan members, contributors in the field, diaspora

All three share **one backend, one database and one review queue**. A word suggested on a phone in Aduku and one suggested on a laptop in London land in the same moderation screen, and once an expert approves it, it is live on the website and in the app at the same moment.

> **Our recommendation: build the website, the admin panel and the mobile app together, on one shared platform, and launch all three within three months.**

Why three months is realistic

We are not starting from a blank page. Kakebe has already built and tested a working demonstrator of this platform for the Lango community (under the working title *Lango Cultural Institution*): more than 30 website page types, 30 managed content types in the admin, about 50 app screens, a documented API, an offline dictionary and an offline contribution queue. The first weeks go into adapting it to the Foundation's identity and filling it with the Foundation's authority, not into discovering what a cultural platform is. Chapters 4 to 6 show it screen by screen.

At a glance

Item	Detail
Scope	Public website, admin control panel and Lango Mobile App (Android, iOS, web app)
Delivery	**3 months (13 weeks)** from signed agreement to public launch: planning, design and modelling, build, content, testing, training and go-live (Chapter 11)
After launch	90 days of included hypercare, then a support plan (Chapter 12)
Languages	English and Leb Lango; interface wording entered by the Foundation's experts, never machine-translated
Ownership	Content, data and accounts belong to the Foundation; custom code is licensed to it; documentation and training included
Investment	Set out in the separate Financial Proposal

What the Foundation gains

- **A trusted public record** of the language, clans, districts and heritage, with sources shown and reviewers named.
- **A Language Hub** that teaches Leb Lango online and offline, and grows through contributions that experts approve.
- **A contribution engine** for words, proverbs, oral histories and sites, captured with GPS, photo and voice, even offline.
- **Transparent giving and programmes**, and **independence**: trained staff, full documentation and no lock-in.
- **A youth skills pipeline**, because the work is done in Lira with trainees from Kakebe's own programmes.

CHAPTER 2

The Foundation's Needs and Our Approach

What the platform must achieve, the challenges it must overcome, and the principles behind every decision.

The Lango live in nine districts (Lira, Apac, Oyam, Kole, Dokolo, Amolatar, Alebtong, Otuke and Kwania) and Lira City, more than two million people at the 2024 census. Leb Lango is spoken in homes, markets and on the radio; English and Kiswahili are used in offices. The Foundation carries the community's identity under the Won Nyaci, so a platform for it is not a marketing website but a **custodial** one: it holds knowledge in trust, shows where each fact came from, and leaves authority over what is published with the people the community recognises.

> **How we wrote this.** We describe the Foundation's needs from public information and from the demonstrator we have built. Points marked **[TBC]** are for the discovery workshop. We would rather ask than assume.

Seven objectives

Preserve the language, clans, history and heritage in a durable, sourced archive · **Teach** words, proverbs and greetings to youth at home and abroad · **Connect** clans, districts and the diaspora · **Represent** the Foundation with an authoritative public reference · **Sustain** programmes, events and giving with visible accountability · **Include** elders and youth, town and village, online and offline · **Govern** with clear roles, review and an audit trail.

The challenges, and how the platform answers them

Challenge	How the platform responds
Knowledge is held in people, not on paper. An elder's passing can take a clan's stories with it	Guided forms for oral history, words, proverbs and sites, with voice, photo and GPS, reviewed and archived
Language shift among youth	Dictionary, English to Leb Lango translator, proverbs, greetings and lessons, usable offline on a phone
A dispersed community and patchy, expensive data	Website for reach, app for daily use, offline-first design, a diaspora corner, a clan picker on every registration
Authenticity must never be in doubt	Sources shown, trust labels, expert review, and nothing invented (Chapter 7)
Paper processes and limited IT capacity	Online forms with tracking codes, a no-code admin, role-based access, training and a support plan
Sensitive public matters	Officeholders and titles published exactly as the Foundation confirms, with an approval step; the platform takes no position
Funding and accountability	Pledges, programme progress and a transparency dashboard

Who the platform serves

Audience	What they need	Where they meet the platform
Youth and students	Learn the language and history, find events, earn recognition	App, website
Elders and knowledge holders	Have their knowledge recorded and respected	Assisted contribution, admin review
Clan leaders	Maintain their clan's page, submit corrections	Clan self-service in the admin, website
Diaspora	Stay connected, learn, give, attend events	Website, app, diaspora corner
Researchers, media, schools	Citable, sourced material and open data	Website, library, open data
Partners and donors	See programmes, progress and transparency	Website, programmes and transparency pages
Foundation staff	Publish, review, report and communicate	Admin control panel

Guiding principles

Community authority (the Foundation decides what is true; the platform never invents culture) · **Offline first** (designed for the weakest connection) · **Plain language** (large touch targets, readable type, simple flows) · **Own your data** (exportable at any time) · **Built to last** (well-understood technology that local developers can maintain) · **Respect for knowledge** (consent, attribution and restricted access from the start).

CHAPTER 3

One Platform, Three Surfaces

Why the website and the mobile app belong together, and how one shared platform gives the Foundation more reach for less effort.

A single platform with **one backend and three surfaces**: a public website for reach, credibility and search; an admin control panel where the Foundation's staff run everything; and the Lango Mobile App for daily use, offline learning and field contribution.

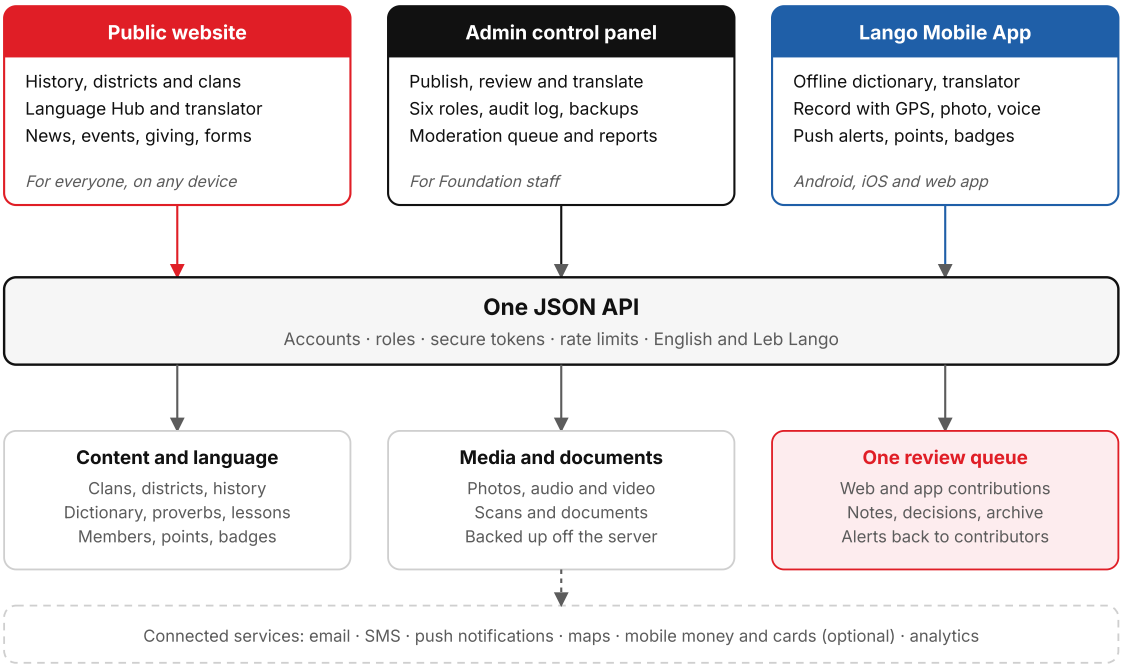


Figure 3.1: One platform, three surfaces. Every surface talks to the same JSON API, database and review queue.

Why not the website alone, or the app alone?

Need	Website	Mobile app
Be found on Google, shared in a link, cited by media	**Strong.** Every page has its own address and share preview	Weak
Read long histories, tables and maps; staff administration	**Strong** on desktop and tablet	Short reading only; not for admin
Work with no internet	Limited (cached pages)	**Strong.** Offline dictionary, queued contributions, saved tickets
Record a voice, photo or GPS point at the source	Possible, clumsy	**Strong.** Native camera, microphone, location
Remind and re-engage people	Email only	**Strong.** Push notifications, word of the day
People who will not install an app	**Strong.** Nothing to install	Installable web app (PWA) covers them

The website is the Foundation's **public face and control room**; the app is its **daily companion and field recorder**. Together they cover every audience.

What "shared" means

One set of accounts (sign in once, on either). **One content store** (a history chapter published in the admin is the same chapter the app shows, in English and Leb Lango). **One review queue** (every contribution, word or proverb lands in the same moderation workspace with the same status model and notifications). **One API**, which any future channel (a kiosk, SMS, a partner portal) can also use. A correction made once is corrected everywhere.

Building the three together costs far less than building them one after the other. If the Foundation prefers to phase delivery, the website and admin can launch first and the app follow, with nothing rebuilt; the scope options and their cost are in the separate Financial Proposal.


CHAPTER 4

The Public Website


A fast, bilingual, brand-led home for the Foundation's history, language, clans and heritage, designed to be read on a phone first.

The site carries the Foundation's own identity: logo, colours, photography and tone. It is mobile first, switches between English and Leb Lango in one tap, targets WCAG 2.1 AA, and has a lightweight mode for slow connections.

Section	What visitors find
Home, About, Leadership	Quick actions, word of the day, mission, the Won Nyaci, cabinet and elders
History	Ten chapters with a table of contents, timeline, glossary and a list of sources
Districts and Lira City	Atlas, comparison table, map, and a page per district (people, economy, places, history)
Clans and notable Langos	A searchable Clan Explorer with a page per clan (totem, district, leader); biographies of notable people
Heritage and biodiversity	Ceremonies, attire and crafts, music and dance, symbols, sites on a map; a species register with a sightings map
Language Hub	Dictionary, English to Leb Lango translator, proverbs, greetings, lessons, "suggest a word"
Library and media	Sourced documents with downloads; photo, video, audio and podcast galleries; 360 degree tours
News, events, programmes	Bilingual news, event registration with printable ticket, programmes with progress and a sponsor button
Get involved and giving	Contribute, volunteer, scholarship, grant, partner, clan registration, diaspora corner; donation pledges and a transparency page
Assistant, search, open data	A question box that answers only from reviewed content, with sources; faceted search; documented open data



The demonstrator home page: quick actions, word of the day, clans, districts, programmes and news.



The dictionary: topic filters, A to Z browsing and a verification status on every entry.

The Language Hub

Search works in both directions and folds special letters, so typing *e* finds *ɛ* and *ng* finds *ŋ* on a plain keyboard. The translator uses the dictionary, not machine translation, and says so. Anyone can suggest a word or proverb: a duplicate check runs, a language expert edits and approves, and the entry appears with a **Community** label until verified. The demonstrator already holds a starter dictionary of 2,829 entries, every one marked *unverified* until the Foundation's experts review it.

Community participation

One simple form lets a visitor contribute a cultural observation, natural heritage sighting, word, proverb, oral history, document or heritage site, with GPS, photos, audio and files, and a **tracking code** to follow it. Accounts earn points, levels and badges. A **clan picker** on every registration, with a "my clan is not listed" option that alerts the administrators, builds the register over time. Search-engine friendly pages, share previews and a newsletter list are included; privacy-conscious analytics are added in this engagement.

CHAPTER 5

The Admin Control Panel

A role-based workspace where the Foundation's own people publish, review, translate and report, with every change recorded and reversible.


The admin is where the platform stays alive after launch, so it is built for the Foundation's staff and volunteers, not for developers: one consistent layout, a live notification bell for every new submission, and every content type edited through the same simple forms.

Six roles


Role	Typical person	Can do
Super admin / Admin	Platform owner, operations lead	Everything, including users, settings and backups
Editor	Communications staff	Create and publish news, pages, history, heritage, events, programmes
Moderator	Language experts, community managers	Review contributions, word suggestions, comments and messages
Clan leader	Verified leader of one clan	Edit their own clan only; changes are reviewed, never self-published
Contributor	Any registered member	No admin access; submits from the website or app

What can be managed

Group	Managed items (30 content types plus bespoke screens)
Culture and language	Dictionary, proverbs, lessons, clans (bulk add and CSV import), districts, notable Langos, history chapters, timeline, glossary, heritage, species, 360 tours
Content and media	News, events, programmes, media, documents, partners
Community and moderation	Contributions, word and proverb suggestions, comments, messages, applications, professionals, subscribers
Finance and assistant	Donations (confirm, export), programme progress; assistant knowledge base and flagged answers
System	Users and roles, branding, **Translations** (the Leb Lango interface, entered by experts, never machine-translated), notifications, audit log, backup, export



The dashboard: items waiting for review, contributions per month, archive at a glance and quick actions.



Reviewing a contribution with its media, location, review note and status actions.

The moderation workspace

This is the screen that protects the Foundation's credibility. A reviewer opens a contribution with its photos, audio and map pin, adds a note the contributor sees, corrects it, then approves, publishes, returns or rejects it. Each action notifies the contributor in the app and by push, awards points, and an approved item can be added to the archive as a permanent record.

Safe by design


Version history with restore; an audit log of who did what and when; forced password change at first sign-in; login throttling and rate limits; CSV and JSON export and a full database backup on demand. After handover the Foundation can run all of this itself; Kakebe is needed only for new features, security updates and infrastructure.

CHAPTER 6


The Lango Mobile App

The whole platform in a pocket: offline dictionary, guided contribution from the field, notifications and recognition, on Android, iOS and the web.


For most people in Lango the phone is the computer. The app does two jobs the website cannot: **daily learning** (word of the day, offline dictionary, phrasebook, translator) and **capturing knowledge where it lives**: an elder's story, a heritage site in the bush, a ceremony in a village, recorded with voice, photo and GPS and sent when the connection returns.




Home: word of the day, points, news, events.




Contribute: seven guided forms.



Dictionary: works offline.



Translator: no machine translation.



Explore: the whole archive.

Tab	What it does
Home and Explore	Greeting, word of the day, points and level; clans, districts, notable Langos, history, heritage, biodiversity, library
Contribute	Seven guided forms (cultural observation, natural heritage, word, proverb, oral history, document, heritage site) with GPS, camera, audio and files; tracking code; works offline
Learn	Dictionary (offline once downloaded), translator, proverbs, phrasebook, suggest-a-word
Connect and Support	Events with tickets, professionals directory, source-bound Cultural Assistant, news; giving pledges and transparency
Me	Points, Bronze to Platinum levels, badges, my contributions and their status, in-app and push notifications

Built to work with no internet

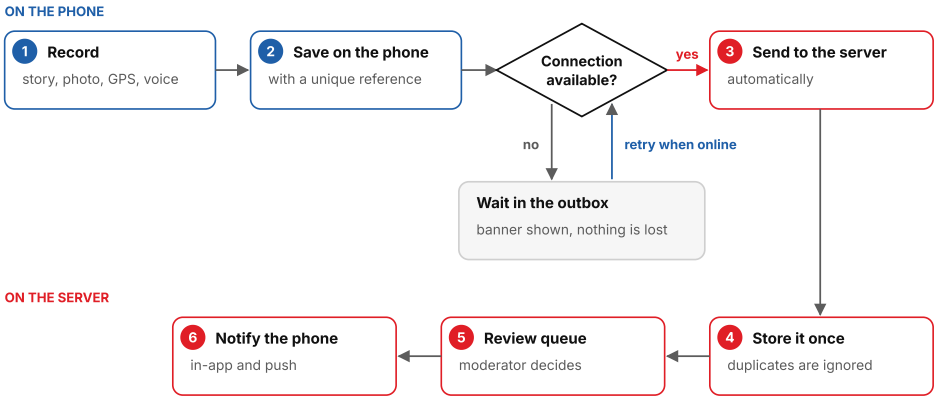


Figure 6.1: Offline-first behaviour. A contribution is saved on the phone, queued, and sent when the connection returns, with a unique reference so it can never be stored twice.

Stale-while-revalidate: every page shows the last saved copy at once and refreshes in the background. **Offline dictionary:** one tap downloads all published words, versioned so an update downloads nothing when nothing changed. **Offline contributions:** photo, audio and files wait in a queue and send automatically, **never duplicated**. Tickets and tracking codes open offline, and the sign-in token sits in the phone's secure store.

Distribution and what comes next

One **Expo / React Native** codebase builds **Android**, **iOS** and an **installable web app** that needs no store, published in the Foundation's own store accounts, in English and Leb Lango. After launch: SMS and USSD fallback, one-time-code sign-in, clan groups, maps and 360 tours in the app, live mobile-money payments.

CHAPTER 7

Contribution and Content Governance

How knowledge enters the archive, who decides what is true, and how the platform protects the Foundation's credibility and its people.

The platform never invents culture. Clans, proverbs, translations, biographies and history come only from the Foundation, from published sources shown on the page, or from community contributions that an authorised reviewer has approved. Where something is missing, the platform shows it as empty, not made up.

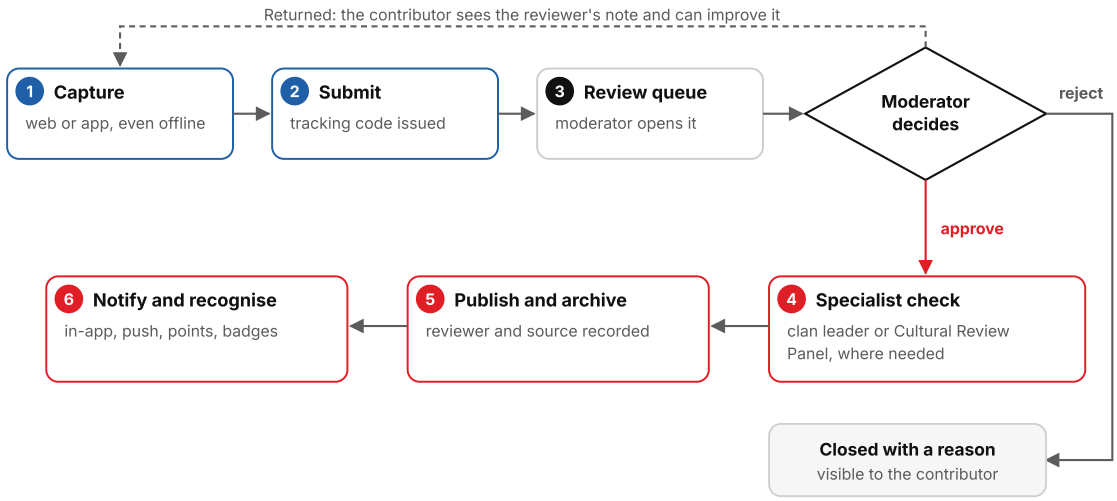


Figure 7.1: The lifecycle of a contribution, from capture on the phone or website to a published, attributed archive record.

A contribution moves through six statuses the contributor can see: *Pending*, *Under review*, *Returned* (with the reviewer's note), *Approved*, *Published* or *Rejected* (with a reason). Anyone can check a submission by its tracking code without logging in. **Moderators** (language experts and community managers) review; **clan leaders** edit only their own clan and cannot publish their own changes; **editors** publish Foundation content; **admins** manage users. We recommend adding a **Cultural Review Panel** of elders and historians as the final reviewer for sensitive content [TBC: panel and categories to be confirmed by the Foundation].

Every record says how far to trust it

Label	Meaning
Verified	Checked and approved by the Foundation's experts
Community	Contributed by a member and approved by a moderator, not yet verified
Unverified	Loaded from a starter source (for example the starter dictionary) and awaiting expert review
Source cited	History, districts and people show the published sources they come from

Cultural protocols (to be agreed at discovery)

Protocol	How the platform supports it
Informed consent	Recording and photo forms record that the speaker or owner agreed to the use of their words and image
Attribution	Credit by name, by clan or anonymously, as the contributor wishes
Restricted knowledge	A record can be held in the archive but shown only to authorised roles, or not at all
Correction and removal	Every page will offer a route to request a correction or withdrawal, handled in the review queue
Children's content	Clear rules and guardian consent for photographs and recordings of children
Neutrality	Leadership titles and officeholders appear exactly as the Foundation confirms; the platform takes no position on disputes

Ownership. The Foundation owns the content and data; contributors keep authorship and grant a licence to publish and preserve. Public reuse as open data is the Foundation's choice. **Abuse controls:** rate limits, duplicate checks, moderation before publication, account controls. **The Cultural Assistant** answers only from the register and reviewed archive, shows its sources, and logs what it cannot answer so the Foundation can fill the gap.

CHAPTER 8

Architecture, Security and Data Protection

Plain, proven technology on affordable hosting, with security and privacy designed in and a clear route to grow.

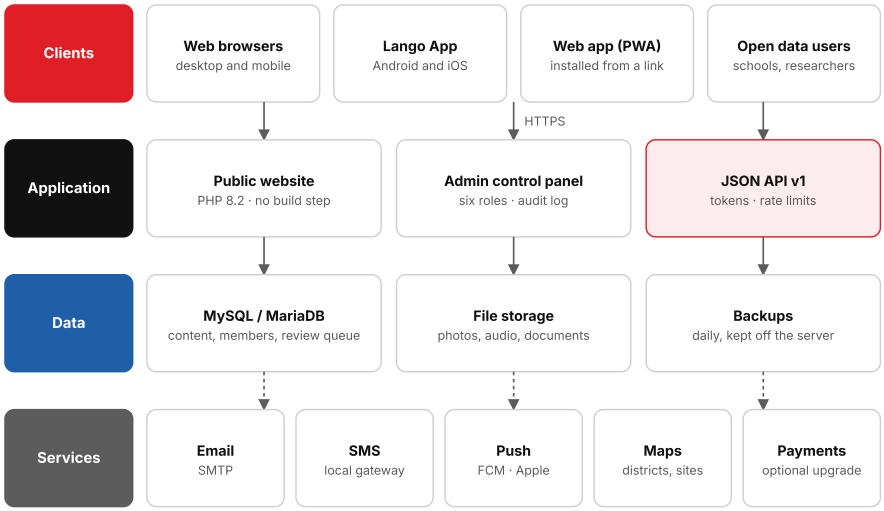


Figure 8.1: Architecture. Three surfaces share one API, one database and one media store; services sit behind the API.

Layer	Choice	Why
Website, admin	PHP 8.2, MySQL or MariaDB, no framework, no build step	Runs on affordable hosting; easy for local developers to maintain; the approach used in several Kakebe systems
API	Stateless JSON API with bearer tokens, paging, rate limits, documented errors	Any future channel can use it
Mobile app	Expo and React Native, one JavaScript codebase; web app from the same code	Android, iOS and web from one build; over-the-air fixes
Services	Push (Firebase, Apple), SMTP email, local SMS gateway, maps; mobile money (ioTec Pay, Pesapal) as an optional upgrade	Already integrated in other Kakebe products

Hosting. Managed by Kakebe, or on the Foundation's own account; staging and production environments; HTTPS mandatory. Domain, hosting and store accounts are in the Foundation's name [TBC: preferred hosting location and domain]. **Backups:** automated daily database backups kept off the server, regular copies of uploads, an on-demand SQL backup, and a restore drill before launch.

Security

In the demonstrator today: hashed passwords; API tokens stored only as SHA-256 hashes; no session cookies on the API; six roles with scoped permissions; rate limits on sign-in, registration, uploads, translator and assistant; duplicate-safe uploads; CSRF protection on forms; forced password change at first sign-in; audit log and version history; secure token storage on the phone (Keychain, Keystore); account deletion. **Added before launch:** HTTPS and security headers, a dependency and configuration audit, input and upload hardening, and a **penetration test** against the OWASP Top 10 by Kakebe's cybersecurity team.

Data protection and privacy

The platform will hold personal data (names, contacts, clan, location, recordings), treated as a duty of care and aligned with the **Uganda Data Protection and Privacy Act, 2019**:

- **Consent and purpose:** plain-language consent at registration and on forms, with a privacy notice in English and Leb Lango; data used only to run the platform and the Foundation's work, never sold.
- **Minimisation:** only the fields needed; phone, country and clan optional where possible.
- **Rights:** members can view, correct and delete their account; administrators can export or erase a person's data on request.
- **Accountability:** a retention schedule, a nominated data protection focal person, and registration with the Personal Data Protection Office [TBC: confirm with the Foundation's legal adviser]. The demonstrator's privacy and terms pages are drafts that we finalise with that adviser before launch.
- **Children and hosting:** clear rules for children's recordings and a disclosed hosting location.

Reliability and inclusion. Caching, uptime monitoring under the support plan, WCAG 2.1 AA, Leb Lango beside English, and assisted contribution so a youth ambassador can record for an elder with consent captured.

CHAPTER 9

About Kakebe Technologies

A youth-led technology company in Lira City that builds software, AI and robotics for real local problems, and trains the next generation to build them too.

Kakebe Technologies Limited is a youth-led technology hub in **Lira City**, in the heart of Lango. For more than five years we have worked with non-profits, government offices, schools, churches, businesses and community groups across Northern Uganda and beyond. **Mission:** build homegrown software, AI and robotics, and teach young people to build the next ones. **Vision:** a Northern Uganda where youth-led innovation solves local problems and Lira City is known for digital talent.

5+ years	257 youth	6 service lines	20+ platforms
building technology in Lira City	graduated from Tech Camp 2025 alone	software, marketing, AI, security, training, internships	websites, portals, ERPs, apps and SaaS delivered or incubated

Service line	How it applies to this project
Software development (web and mobile apps, APIs)	The website, admin, API and app
Digital marketing (SEO, social, analytics)	Launch campaign, discoverability, audience growth
Robotics and AI	The source-bound Cultural Assistant and translator; future speech and language tools
Cybersecurity (audits, threat assessment, data protection)	Pre-launch penetration test; data protection design
Tech training	Training the Foundation's team; a digital skills pipeline for Lango youth
Internship programmes	Supervised interns who help with content entry and digitisation

Programmes. *Kakebe Tech Camp* is a residential bootcamp for ages 13 to 30 in robotics, AI, web and app development, entrepreneurship and multimedia; Camp 2025 trained **257** young people from across East Africa, and the next camp runs on 14 to 23 December 2026. The *Digital Bridge Internship Programme* puts interns on live projects with a certificate at the end. The *Innovation Programme*, home to the **Lango Innovation Challenge** and regular Tech Talks, incubates young innovators; several of our own products began there.

The team

Name	Role	On this project
Sedrick Otolo	Team Lead	Leads the team and the client relationship; accountable for delivery
Patrick Okello	Chief Technology Officer	Technical direction, architecture and quality
Oscar Jerome Okello	Web Development Lead	Leads the website and admin build
Komakech Moses	Sales and Marketing	Stakeholder engagement, launch communications and training coordination
Bodo Desderio	SEO Engineer	Search visibility, content structure and analytics

Why Kakebe

We are local: our office is in Lira, so workshops with elders, clan leaders and language experts happen in person. **We have already built it:** the demonstrator is a working version of this proposal. **We have proven delivery** of every technology involved: content-managed sites, multi-role admin systems, mobile apps on a shared API, offline-first design, mobile-money payments, tracking codes and government work (Chapter 10). **We build capacity, not dependency:** staff are trained, documentation is complete, and the content and data belong to the Foundation. **We keep the money and the skills in Lango. We are accountable:** fixed milestones, a staging site to review at any time, and a named team.

CHAPTER 10

Portfolio and References

Platforms we have designed, built and operated, and what each one proves about our ability to deliver the Foundation's website and app.

Where a system serves confidential or government users we describe it in words and offer a private demonstration with the client's permission. [TBC: Kakebe to confirm which clients agree to act as referees.]

Reference projects

Project	What we built	Why it matters here
Lango cultural platform (demonstrator)	Website, admin, API and mobile app, working end to end	The complete solution, already built
A Better Life International (betterlifeint.org)	Redesigned site with a BetterLife Farm shop, a full admin (programmes, team, impact figures, reports, blog, orders), card and mobile-money checkout through Pesapal	A foundation website run by non-technical staff, with payments
Betty Amongi Foundation	Foundation website with a CMS area (posts, pages, gallery, comments, messages) and a mentorship portal with participant, mentor and admin areas	A foundation serving the same Lango community
Pure Wage Foundation	[TBC: scope and URL]	[TBC]
Civic Coded	[TBC: scope and URL]	[TBC]
OPM Schedules (Office of the Prime Minister scheduling application)	Multi-tenant scheduling for ministry offices of the Government of Uganda: meetings and trips, clash flags, branded email reminders, weekly programme as PDF, super-admin onboarding	Government-grade role separation, notifications, branded PDFs
iRecover	Lost-documents recovery: public search and report, matching, mobile-money recovery fee, partner-station and admin dashboards, receipts with pickup codes	Tracking codes and a multi-party review workflow
BodaERP (in development)	Rider registry, fee collection and compliance across riders, stage chairpersons, city councils, government and admins; ID cards, audit logs, data-quality flags	A five-role registry like the clan register
FaithFellows (web and mobile app)	Multi-tenant church platform: sites, sermons with offline listening, Bible, live streaming, giving by mobile money, prayer wall; Laravel web and Expo app on one API; English, Luo, Luganda, Swahili	The Lango App's architecture, in production
Soila (in development)	An AI app that helps farmers test soil and grow better	AI and rural mobile experience
Better Life Farmers Connect	[TBC: scope and URL or store link]	[TBC]
Lira City website	Rebuild of the city site with a CMS, tenders, downloads, FAQs and citizen issue reports with tracking codes	A public institution in Lira; tracking codes
SignConnect Uganda	Sign-language learning app: tagged videos, lessons, classes with join codes, parent profiles, WCAG 2.1 AA, offline lessons	The nearest cousin to the Language Hub
ObiFunds, ObiTickets, ChamaFunds	Crowdfunding (www.obifunds.com), QR event ticketing with a gate scanner, community fundraising; mobile money in and out	Giving, tickets, receipts and payouts

More delivered work

- **Kakebe Tech Camp platform:** registration, ioTec payments, PDF receipts, QR ticket, participant portal
- **KPOS:** multi-tenant point of sale, MoMo and Airtel, English, Luganda, Kiswahili
- **Falcon ERP:** four-role export pipeline with geotagged checkpoints and signed delivery notes
- **Mwonya Streams** (mwonya.com): streaming for local culture and indigenous voices
- **Kakebe Shop Online** (kakebeshop.com): an online shop for Northern Ugandan businesses
- **Oroma TV:** news, shows and live streams for Northern Uganda
- **Innovate2Day:** opportunity hub for young African innovators with an AI-assisted admin
- **NUFA and NUFA Awards:** Northern Uganda Filmmakers Association sites
- **Mighty Rides:** Next.js website and portals with a Laravel accounting back office
- **Kakebe Management System:** people, programmes, projects, finance and impact
- **NursesPro Academy:** e-learning for nursing and midwifery students
- **School sites:** Es Shemen International School, Kiryandongo High School
- **Corporate sites:** H. Tubman Solutions, Bellan Contractors, Nilotica Shea
- **Heritage and advocacy sites:** Big Five Heritage Collection, Denise Ayebare

[TBC: Kakebe to confirm this list and any client permissions before the proposal is sent.]

Three references in more detail

FaithFellows: the Lango App's architecture, in production. One Laravel backend serves church websites and an Expo / React Native app through the same API, in English, Luo, Luganda and Swahili, with an installable web app, a lite mode for slow connections, offline listening, push notifications and moderated community features: the same combination this platform needs.

SignConnect Uganda: a community's language, taught on a phone. Short tagged sign videos with slow motion and repeat, captions, lessons, classes with join codes, parent profiles and progress, bulk upload for admins, designed to WCAG 2.1 AA. It is the closest cousin to the Language Hub.

Lira City website and iRecover: tracking codes and review workflows. Citizens report an issue or a lost document, receive a tracking code and follow it through staff review: the pattern the contribution engine reuses for the Foundation.

What the Foundation needs, and where we have delivered it

Requirement	Delivered in
No-code content management	A Better Life International, Betty Amongi Foundation, Lira City website, NUFA, Innovate2Day
Multi-role access and approvals	OPM Schedules, BodaERP, iRecover, FaithFellows, Lira City website
Mobile app and web sharing one API; offline use	FaithFellows, SignConnect Uganda, KPOS
Mobile money and card payments	ObiFunds, ObiTickets, iRecover, BodaERP, KPOS, Tech Camp, ChamaFunds, A Better Life International
Events, ticketing and QR check-in	ObiTickets, Kakebe Tech Camp, FaithFellows
Public reporting with tracking codes	Lira City website, iRecover
Local-language interfaces	FaithFellows (Luo, Luganda, Swahili), KPOS (Luganda, Kiswahili)
Audio, video and live streaming; lessons	FaithFellows, SignConnect Uganda, Oroma TV, Mwonya Streams, NursesPro Academy
Dashboards, PDF and spreadsheet reports	KPOS, ObiFunds, BodaERP, OPM Schedules
GPS, photo and signature capture in the field; AI features	Falcon ERP; Soila, Innovate2Day AI Writer

CHAPTER 11

Delivery in Three Months

Planning, design and modelling, build, content, testing and launch in 13 weeks, with a staging site the Foundation can review from week 3 and fixed gates before anything goes public.

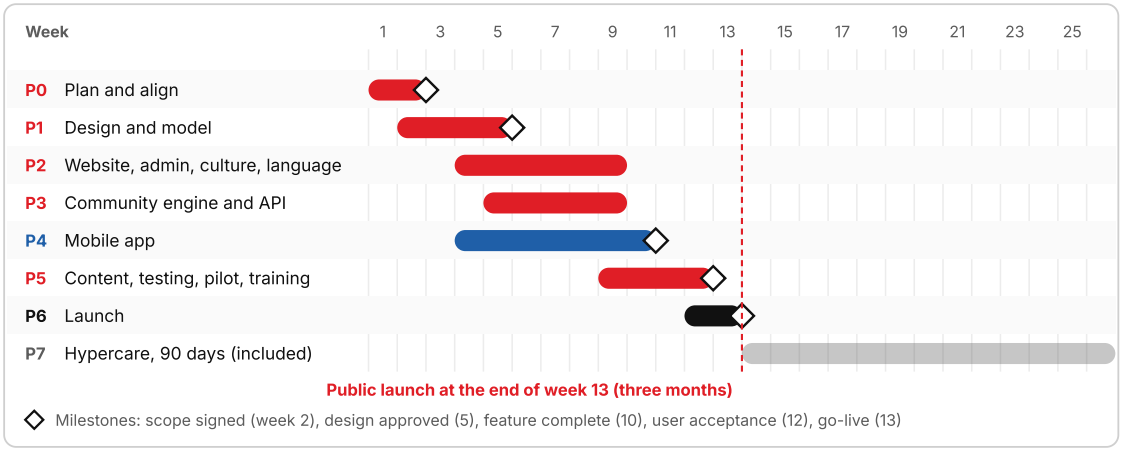


Figure 11.1: Three-month plan. Public launch at the end of week 13; 90 days of hypercare follow, included.

Phase	Weeks	What happens	Gate
P0 Plan and align	1 to 2	Kick-off, workshops with leadership, language experts, historians and clan leaders; content audit; review of the demonstrator; roles and scope confirmed	Scope and plan signed
P1 Design and model	2 to 5	Brand and interface design, clickable prototype, data and content model, hosting and staging set up; admin roles agreed	Design approved
P2 Build	4 to 10	In parallel streams: website, admin, culture and language modules; community engine and API; the mobile app with offline dictionary, outbox and push	Feature complete
P3 Content, testing, pilot, training	9 to 12	Content loaded and verified; functional, device, offline, accessibility, performance and security tests; pilot with 20 to 40 users from different districts; staff, moderator and clan-leader training	Acceptance signed
P4 Launch	12 to 13	Store submissions (Android first, then iOS; web app from day one), production go-live, launch communications	Go-live approved
Hypercare	90 days after launch	Daily monitoring, rapid fixes, usage reviews at 30, 60 and 90 days, hand-over to a support plan	Hypercare report

How we work

Two-week cycles end with a demonstration on the staging site, so feedback goes straight into the next cycle. A **weekly 30-minute call** with a one-page status report, and a **monthly steering meeting** for leadership. One visible **backlog**, with change control: requests beyond the agreed scope are estimated and approved in writing before work starts. A feature is **done** only when built, tested on real devices, documented and accepted by the Foundation's coordinator.

Content is a work stream

We **audit** what exists (registers, dictionaries, histories, photographs, recordings), agree a **minimum launch set** in week 2, prepare templates and CSV formats, **bulk-load** clans, dictionary entries and proverbs, and have the Foundation's panels **verify** them, with supervised interns helping with entry. The Foundation's verified content is never overwritten by updates.

Quality and launch

Testing covers function, low- to high-end Android phones and iPhones, offline use, accessibility, performance on a throttled 4G connection, security (OWASP Top 10) and language (spelling, diacritics, bilingual consistency). No critical or high defect may remain open at go-live. Launch is a **soft launch** to the pilot group, then public, with a communications pack: press release, social assets, short how-to videos in English and Leb Lango, and posters with QR codes [TBC: launch event date and venue].

> **What makes three months possible:** the working demonstrator, a named Foundation coordinator in week 1, reviews within five working days, and a minimum launch content set agreed in week 2. If any of these slips, we say so early and re-plan together.

CHAPTER 12

Team, Governance, Training and Support

Who does what on both sides, how decisions are made, how the Foundation's people are trained, and how the platform is looked after once it is live.

Foundation side	Role in the project	Time needed
Executive sponsor	Champions the project, resolves escalations, approves milestones	A few hours a month
Project coordinator	Day-to-day decisions, gathers feedback, signs off deliverables	About 4 hours a week
Language committee and history and heritage panel (elders, historians)	Review Leb Lango wording, the dictionary, history, clan and heritage content	Scheduled review sessions
Clan leader liaison, communications officer, finance officer, data protection focal person	Validate the clan register; supply brand assets and news and become the lead editor; set up giving; handle privacy requests	As needed; the communications officer about 2 days a week after launch

[TBC: the Foundation to name an individual for each role in the first week.] On Kakebe's side Sedrick Otolo leads delivery, Patrick Okello owns architecture, security and quality, Oscar Jerome Okello leads the website and admin, Komakech Moses leads engagement and training, Bodo Desderio leads search and analytics, with a mobile lead, a product designer and a QA engineer [TBC: names] and supervised interns for content entry.

Governance. A monthly steering meeting (sponsor, coordinator, Kakebe lead and CTO), a weekly project call, a demonstration every two weeks and a one-page weekly status report. Issues go first to the coordinator and the Kakebe lead, then to the steering group within three working days. The sponsor approves scope, design and go-live; the coordinator accepts deliverables; the language and history panels own the cultural content; Kakebe owns build, testing and security.

Training and handover

Audience	Session	Outcome
Administrators	1 day, hands-on, in Lira: roles, users, settings, backups, exports	Can manage users, settings and data
Editors and communications	1 day: news, pages, events, media, translations, SEO basics	Can publish and maintain content
Moderators and language experts	1 day: review queue, dictionary and proverbs, translations	Can review and approve with confidence
Clan leaders and youth ambassadors	Half day each, in English and Leb Lango: clan self-service; assisted contribution with consent	Can maintain a clan page; can record for an elder

Materials: an administrator manual, short videos, quick-reference cards in English and Leb Lango, a moderator checklist. Two or three Foundation staff are trained as trainers. At **handover** the Foundation receives the deployment process, access to hosting, domain, database and store accounts in its name, technical and user documentation, a content inventory with the sources behind every loaded fact, and a maintenance runbook.

Support after launch

Hypercare is included for the first 90 days: daily monitoring, rapid fixes at no charge, usage reviews at 30, 60 and 90 days, and training clinics. After that the Foundation chooses a **support plan** (Essential, Standard or Premium) covering uptime monitoring, security updates, daily backups with restore tests, defect fixes, app-store and operating-system updates, and a quarterly review of the roadmap. Response times by severity (critical, high, medium, low) and the availability target are fixed in the support agreement; plan prices are in the Financial Proposal. The Foundation owns its code licence, content, data, domain and store accounts, and can export everything in standard formats at any time, so it stays with Kakebe because the service is good, not because it is locked in.

CHAPTER 13

Risks, Success Measures and Assumptions

What could go wrong and what we do about it, how the Foundation will know the platform is working, and the conditions the three-month plan depends on.

Risk	Mitigation	Owner
Disputed or inaccurate cultural content damages trust	Sources shown, trust labels, Cultural Review Panel, nothing published without approval, officeholders shown as the Foundation confirms	Foundation sponsor
Content arrives late or incomplete	Content audit in week 1, minimum launch set agreed in week 2, bulk import tools, supervised interns	Foundation coordinator
Reviews are slow (a three-month plan has no slack)	Named roles in week 1, five-working-day review rule, fortnightly demonstrations, decision log	Both coordinators
Low connectivity limits use	Offline-first app, versioned offline dictionary, lite web mode, queued uploads	Kakebe technical lead
Low adoption after launch	Launch plan, youth ambassadors, clan-leader onboarding, events, recognition, regular content	Foundation communications
Spam, abuse, privacy breach, data loss	Moderation before publication, rate limits, security review and penetration test, encrypted connections, backups with restore tests	Kakebe technical lead
App-store delay or rejection	Early account set-up, guideline review, web app live from day one, Android first	Kakebe mobile lead
Scope creep	Agreed scope, single backlog, change control, a roadmap for later phases	Kakebe project lead
Running costs unfunded, leadership changes	Costs shown openly in the Financial Proposal; governance by role, not individual; neutral presentation of officeholders	Foundation sponsor

Measuring success

A short set of indicators, linked to the seven objectives, shown on the admin dashboard and reviewed monthly by the coordinator and quarterly with Kakebe; baselines and targets are agreed at discovery [TBC]. They count activity, not individuals: **records in the archive** and the **share marked verified**; **oral histories** captured; **dictionary searches** and offline downloads; **members** by district, clan and country; **monthly active users** and installs; **contributions per month** and the median time to a decision; registrations, tickets and giving; staff who can run the platform unaided; uptime.

Assumptions, dependencies and exclusions

- The Foundation names its coordinator and panels in week 1, gives feedback within **five working days**, supplies its logo, colours and photographs by the end of week 2, and arranges the pilot of 20 to 40 users.
- Cultural, historical and language content is supplied or verified by the Foundation's experts; Kakebe structures, loads and formats it. The platform is delivered in **English and Leb Lango**; other languages are quoted separately.
- Store accounts (Google Play, Apple Developer), the domain and hosting are in the Foundation's name; its legal adviser reviews the privacy notice, terms and contributor licence.
- **Not included unless agreed in writing:** writing or translating original cultural content, professional photography or video, large-scale scanning, live payment integration and gateway fees, SMS and USSD, an open forum, printed materials, legal advice, and third-party fees (hosting, domain, store accounts, SMS credits) paid by the Foundation at cost.
- **Intellectual property:** content and data belong to the Foundation; contributors keep authorship and grant a licence; custom code is licensed to the Foundation without time limit [TBC: final wording with the Foundation's legal adviser]; Kakebe's pre-existing components and open-source libraries stay under their own licences. Each party keeps the other's confidential information private.
- A deliverable is **accepted** when it meets its documented criteria with no critical or high defects open and the coordinator signs it off.

CHAPTER 14

Next Steps and Acceptance

From reading this proposal to a signed agreement and a start date, in five steps.

Step	What happens	Who	Target
1. Review	The Foundation reads this proposal, and the Financial Proposal that accompanies it, and notes questions	Foundation leadership	[TBC: date]
2. Demonstration	A live walk-through of the demonstrator: website, admin panel and app on a phone	Kakebe	At the workshop
3. Discovery workshop	90 minutes with leadership and a working group of language experts, historians and communications staff to confirm objectives, scope, roles, content and timing	Foundation and Kakebe	[TBC: date]
4. Agreement	Kakebe issues the final scope and quotation; both parties sign	Both	Within [TBC: 5 to 10] working days of the workshop
5. Kick-off	Week 1 begins: coordinator and panels named, first deliverables scheduled	Both	[TBC: start date]

Questions for the workshop

1. Who will be the **project coordinator**, and who will sit on the **language committee** and the **history and heritage panel**?
2. What **existing content** is there (registers, dictionaries, histories, photographs, recordings), who owns it, and who can approve it?
3. What are the **cultural protocols** for restricted knowledge, recordings of elders and photographs of children?
4. What **identity** will the platform carry (name, logo, colours, domain), and how should **leadership and officeholders** be presented?
5. Which **recognition features** (points, levels, leaderboard) should be public, and is **live payment** wanted at launch or later?
6. Which **dates** (festivals, anniversaries, funding deadlines) should the launch align with, and which partners or institutions should be informed?

Acceptance of this proposal

By signing, the parties confirm that they wish to proceed on the basis of this proposal and the accompanying Financial Proposal, subject to the final agreement.

Item	For the Foundation	For Kakebe Technologies Limited
Name and title	[TBC]	[TBC]
Signature		
Date		

Contact

Kakebe Technologies Limited, Rm B1, Plot 43, Renzo City House, Obote Avenue, Lira City, Uganda · +256 777 676 206 · +256 393 249 845 · service@kakebe.tech · www.kakebe.tech · Proposal contact: [TBC: name, title, direct phone and email].

Thank you for the opportunity to propose. We would be proud to build this with the Foundation, in Lango, for Lango.
